PROJECT PROPOSAL
AI MEETING SECRETARY
FOR JERELRY ORDERS

PROJECT PROPOSAL

Project Name: AI Meeting Secretary for Jewelry Orders – Enhanced Form Filling & Summary Capabilities
Prepared by: DanaExperts
Date: January 16, 2026
Prepared by: DanaExperts
Contact Person: Toan Nguyen
Email: toan.nguyen@danaexperts.com
Phone: (+84) 868-996-897

1. Project Overview

- **Product Name:** AI Jewelry Order Assistant
- **Description:** An AI-powered virtual meeting secretary tailored for Royi Sal Jewelry's OEM and ODM workflows. The system processes inputs from meetings (audio/video), emails, and chats to:
    - Transcribe and summarize key discussions
    - Extract relevant data and map values to the predefined lists
    - Automatically populate the **New Design Requirements Form (S-DV-01 Rev00)** with accurate selections
    - Generate a structured capability summary table for the **ODM-OEM Requirement Form** covering the 25 key fields (Metal, Function, Dimension, Ring/Bangle Size, Chain Type, Chain Length, Chain Extension Length, Logo Metal Purity Location, Logo Brand Location, Tag, Setting Type, Stone Type, Stone Size, Required Weight, Plating, Plating Thickness, Plating Color-Shade, Finishing, Enamel, Enamel Color, Enamel Type, Earring Post Spec, Earring Butterfly Spec, Earring Hook Spec, Jump Ring Spec) with columns:
        - Item/Subject
        - Request Capability (Needed)
        - Request Estimate Cost (Needed)
        - Request 2D Sketch (Needed)
        - Request 3D CAD (Needed)
        - Request Approved Sheet (Needed)

MVP Core Deliverables:

- Fully and accurately filled S-DV-01 form (PDF or digital format)
- ODM-OEM Requirement capability summary table (Excel/CSV or embedded in report)

This solution greatly reduces manual data entry, eliminates errors, speeds up the design-to-production process, and supports Royi Sal's commitment to precision, quality, and long-term partnerships.

- **Development Phase:** MVP – focused on accurate form filling and ODM-OEM capability table generation
- **Collaboration Model:** Agile development with bi-weekly sprints and regular feedback from Royi Sal's DV, Production, and Design teams

2. Proposed Solutions

We recommend two strong technical approaches for the MVP. Each solution is presented in detail below, including technology stack, advantages & disadvantages, estimated timeline, and cost.

Solution 1 – Cloud-Based AI Pipeline (Recommended)

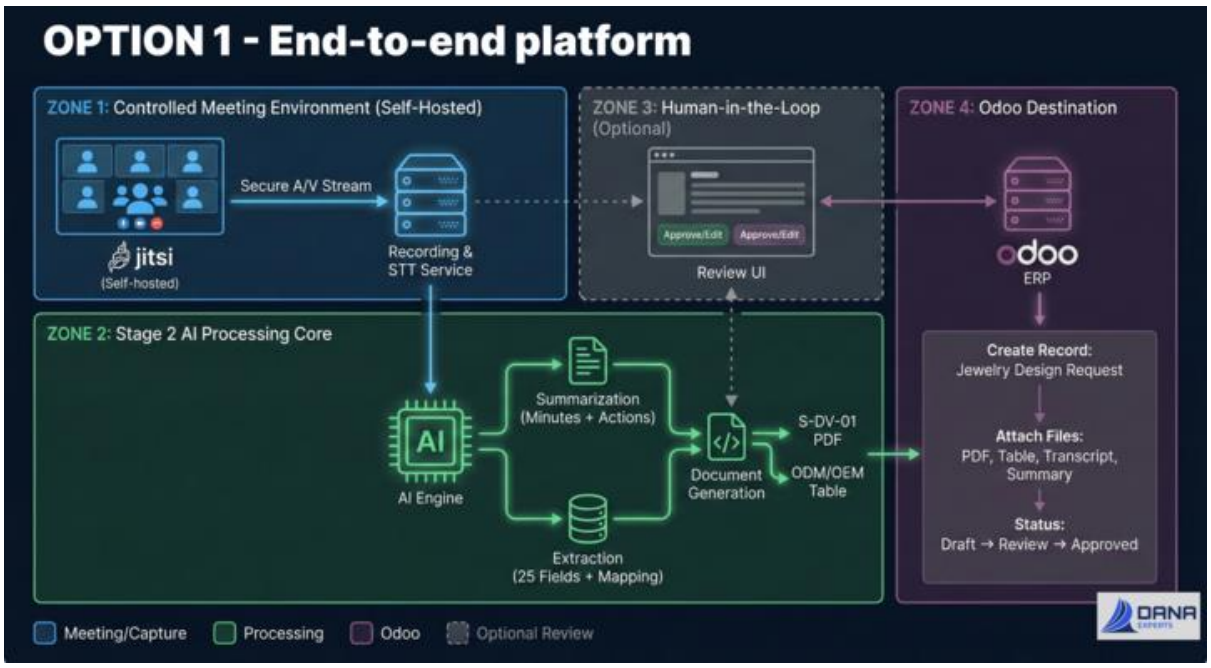

Technology Stack

- Frontend: Web and Mobile Clients
- Backend: Python + Flask (orchestration & processing)
- AI Engine: OpenAI Whisper (speech-to-text) + GPT-4 (summarization, entity extraction, table generation)
- Form & Table Processing: PyPDF2 (S-DV-01 PDF population) + Pandas (ODM-OEM table generation)
- Authentication: JWT-based
- Hosting: Self-hosted, AWS or Google Cloud (scalable & reliable)

Advantages & Disadvantages

Advantages	Disadvantages
Fastest time-to-value (quick MVP deployment)	Dependency on cloud API services (small risk of occasional downtime or rate limits)
High accuracy (90–95%) for both form & table	Requires careful prompt engineering for jewelry-specific terminology
Pay-per-use pricing model keeps initial costs low	
Excellent multilingual support (English/Thai)	
Very easy to scale and extend in future phases	

Estimated Development Time 2–3 months

Project Timeline – Solution 1

Sprint Phase	Duration	Main Focus
Sprint 0	Week 1-2	Requirements refinement, tech setup, prototype transcription & extraction
Sprint 1–2	Weeks 3–7	Core AI pipeline, Odoo integration
Sprint 3	Weeks 8–10	Dashboard development, user testing & refinements
Final	Week 11-12 (if needed)	Optimization, final QA & deployment

Cost Estimation – Solution 1

Item	Hours	Rate	Cost (USD)
Development (AI + Fullstack)	960	$15/h	14,400
Additional Costs (cloud/API/tools)	-	-	1,200
Contingency (10%)	-	-	1,200
Total Estimated Cost			**16,800**
Discount Offer(20%)			**13,440**

Solution 2 – Custom ML Model with On-Premises Deployment

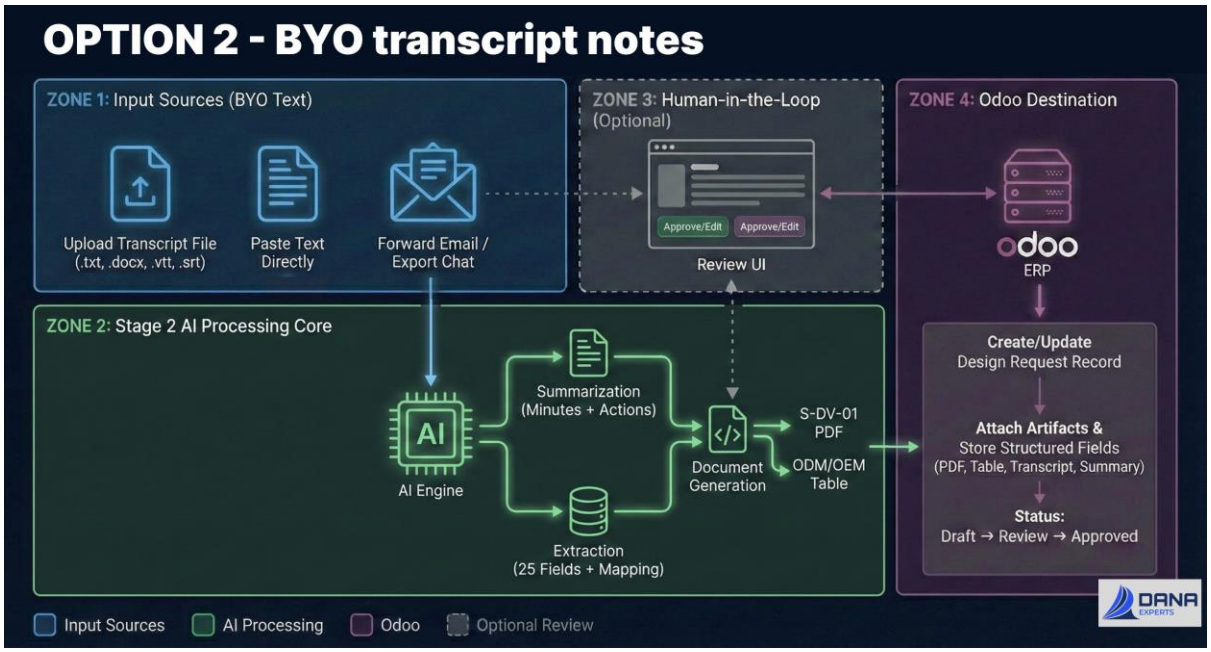

Technology Stack

- Frontend: Vue.js (robust dashboard for input management, review & approval)
- Backend: Django (Python) – secure, enterprise-grade processing
- AI Engine: Fine-tuned Whisper model (STT) + fine-tuned BERT or Llama (high-precision NER & structured extraction)
- Form & Table Processing: Camelot/Tabula (PDF parsing & filling) + Pandas/Openpyxl (ODM-OEM table output)
- Authentication: JWT-based

- Hosting: On-premises server or dedicated AWS EC2 instance (full data control)

Advantages & Disadvantages

Advantages	Disadvantages
Highest possible accuracy (95%+ after fine-tuning)	Longer development timeline due to model fine-tuning & validation
Superior data privacy & security (on-premises)	Higher upfront investment (training data + infrastructure)
Maximum customization for jewelry workflows	Requires more ongoing infrastructure management
Strong long-term maintainability	

Estimated Development Time 8–12 weeks

Project Timeline – Solution 2

Sprint Phase	Duration	Main Focus
Sprint 0	Weeks 1–2	Requirements refinement, tech setup, data preparation & initial fine-tuning
Sprint 1–4	Weeks 3–10	Core AI pipeline, model fine-tuning, S-DV-01 form filling, ODM-OEM table generation
Sprint 5–6	Weeks 11–14	Dashboard development, extensive testing & refinements
Final	Weeks 15–16 (if needed)	Security audit, optimization & deployment

Cost Estimation – Solution 2

Item	Hours	Rate	Cost (USD)
Development (AI + Fullstack)	800	$15/h	12,000
Additional Costs (server/training/tools)	-	-	2,500
Contingency (10%)	-	-	1,200
Total Estimated Cost			**15,700**
Discount Offer(5%)			**14,915**

3. Scope of Work

Category: Backend Development

- Multi-input ingestion (audio, email, chat)
- Transcription, summarization, entity extraction
- Validation & mapping to predefined lists
- Odoo Integration, form generation, summary table generation (25 fields × 5 capability columns)

Category: Frontend Development

- Intuitive dashboard for input upload, review, editing & approval of both forms/tables

Category: AI Feature Enhancements

- Multi-language STT & NLP
- Structured logic to determine "Needed" for each capability column
- Ambiguity resolution & confidence scoring

Category: UI/UX Design

- Tailored for jewelry design workflows
- Clear previews of filled forms
- Highlighting of missing or low-confidence fields

Category: Testing & Optimization

- Comprehensive accuracy testing (target ≥ 93% overall)
- Performance optimization for typical 30–60 min meetings
- Data privacy & security review

4. Feature Estimation

Total Estimated Points: **140**

Epic / Feature Module	Points	Notes
Multi-Input Processing & Transcription	30	Audio (meetings) + text (email/chat) handling
Summarization & Entity Extraction	35	Extract 25+ fields + logic for capability assessment
S-DV-01 Form Auto-Filling & Validation	25	PDF/digital output with predefined list mapping
ODM-OEM Requirement Summary Table Generation	25	25 items × 5 columns (Capability/Cost/Sketch/CAD/Approval)
User Dashboard & Review Tools	15	Approve/edit both forms/tables
Testing & Deployment	10	Comprehensive QA + MVP deployment

5. Payment Schedule

- **Deposit:** 20% upon project kick-off
- **Milestone Payment:** 40% after core functionality delivery (mid-sprints)
- **Final Payment:** 40% upon MVP acceptance and deployment

Monthly invoicing is available based on actual progress.

Closing

DanaExperts is committed to delivering high-quality, practical AI solutions that directly support Royi Sal Jewelry's mission of precision craftsmanship, innovation, and long-term partnerships.

We strongly recommend Solution 1 – Cloud-Based AI Pipeline as the optimal MVP approach. It offers the best balance of:

- Fast delivery (4–6 weeks)
- High accuracy for both S-DV-01 form and ODM-OEM capability table
- Very competitive cost
- Excellent foundation for future expansions (Odoo integration, advanced analytics, etc.)

We are ready to begin immediately. Please let us know which solution you prefer or if you have any additional requirements so we can finalize the project plan and timeline.

I look forward to a successful collaboration!
